afes.
SOFTWARE BUILT BY EXPERTS

MiKU Powered by Mili Express

COMMERCIAL PROPOSAL

Miku Parcel Web Platform

Domain Centralisation & Search Visibility

A public website with parcel tracking, one set of systems under two Miku-owned domains, and SEO and GEO so Miku is found on search engines and AI assistants.

PREPARED FOR

Miku Parcel
Powered by Mili Express
Attn: Muhammad Hamizan bin Ziani

PREPARED BY

afes.
Business Development
Rahimi Rusyuddin bin Mohd Nazri

DATE

26 October 2026

afes.
SOFTWARE BUILT BY EXPERTS

Miku Powered by Mili Express

afes.
Business Development
Remote-first · Global
admin@afes.my
Reg. No. 003865108-P

Date: 26 October 2026

PRIVATE & CONFIDENTIAL · COMMERCIAL PROPOSAL

Muhammad Hamizan bin Ziani
Miku Parcel (powered by Mili Express)

RE: PROPOSAL — MIKU PARCEL WEB PLATFORM, DOMAIN CENTRALISATION & SEARCH VISIBILITY

Dear Muhammad Hamizan,

Thank you for the opportunity to support Miku. This proposal sets out what afes. will deliver to give Miku a modern public website, a single set of systems that Miku fully owns and controls, and the search visibility to be found by customers on both traditional search engines and AI assistants. It covers scope, deliverables, schedule, responsibilities, support and investment, and is intended to be confirmed by both parties before work begins.

At a Glance

#	AREA	WHAT MIKU RECEIVES
1	Public Website	A branded landing page with Track & Trace on **mikuparcel.com**, following the proven layout of leading courier tracking pages.
2	Centralisation	All current systems brought under two Miku-owned domains — **mikuparcel.com** (public) and **mikucentre.com** (management) — with data moved from Qylex Solution to a new database on Exabytes.
3	SEO & GEO	Search Engine Optimization and Generative Engine Optimization, so Miku is found on Google and cited by AI assistants.
4	Timeline & Investment	Final handover by **25 December 2026**. Fixed fee of **RM4,300**, including **3 months of maintenance** at no extra charge.

1. Background & Objectives

Miku is a parcel collection point for students: couriers deliver parcels addressed to the university to Miku, and students collect them there for a collection charge. The website therefore serves students first, helping them check on a parcel, understand the charges and know how to collect.

Miku's current systems are spread across several places. Some sit under Miku's own hosting, others are held by an outside vendor, Qylex Solution, and the rest by further third parties. This makes it hard for Miku to know exactly what it has, who can change it, and where its data lives. It also splits the brand and weakens search ranking, because customers and search engines meet several unconnected properties instead of one.

This engagement has four objectives:

- **One brand, one front door.** A single public website customers can trust and use to track a parcel.

- **Full ownership.** Every domain, hosting account and database registered in Miku's name, with no dependency on an outside vendor for access.
- **Clear separation of public and private.** Public services on one domain, internal management tools on another.
- **Discoverability.** Strong visibility on search engines and AI-driven answer engines.

2. Scope of Work

2.1 Public Website & Landing Page — mikuparcel.com

afes. will design and build the public website using the J&T Express tracking page as a reference for layout and interaction. We follow the pattern, not the content or branding: the site will carry Miku's identity throughout.

- **Track & Trace.** A prominent waybill search bar on the landing page that accepts several waybill numbers at once (separated by commas, up to 10) and returns tracking status from the migrated database.
- **Hero and call-to-action section.** A promotional block (for example, notification sign-up or app download) linking to a destination Miku nominates.
- **Navigation and footer.** Clear header navigation and a structured footer of service and information links.
- **Supporting pages.** Collection Rates, Collection Guide, Outlet Locator, FAQ, Complaint, Claim Support, Internship, About Us and History (see Appendix A). Miku supplies the content; afes. structures and publishes it.
- **Quality.** Fully responsive on mobile, tablet and desktop, fast loading, and built to accessibility best practice. The site is in English.

2.2 Centralisation & Migration — Two Domains, One Owner

afes. will audit every system Miku currently runs, then consolidate them under two domains, both registered to and controlled by Miku:

- **mikuparcel.com** — all public-facing sites and services.
- **mikucentre.com** — private management use only: administration, staff and operations tools. This domain is access-restricted and excluded from search engine indexing.

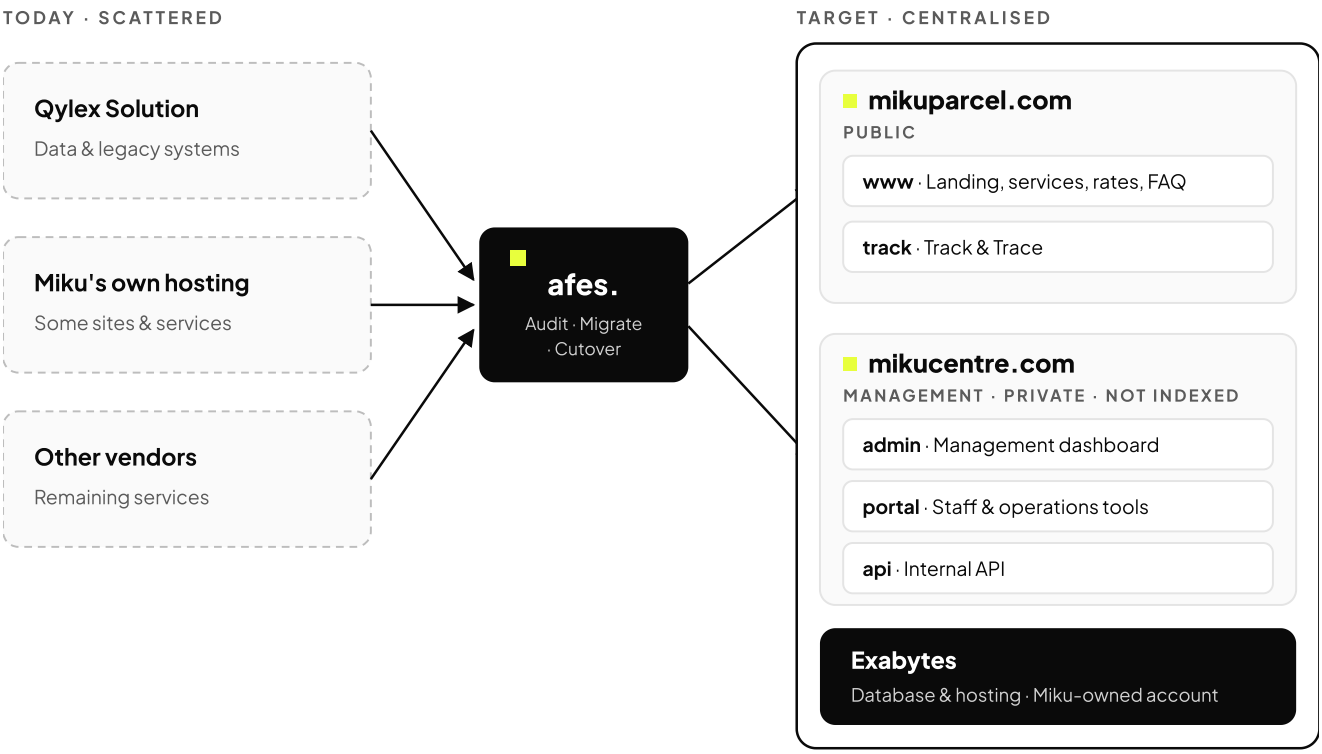


Figure 1 — Proposed domain architecture. Subdomain names are indicative and will be confirmed during Discovery.

The migration covers the following:

- **Audit.** A full inventory of Miku's domains, hosting, databases, email and third-party services, recording who owns and controls each (Appendix B).
- **Data migration.** Moving data held by Qylex Solution to a new database on Exabytes, with validation that records match before and after.
- **Infrastructure.** DNS, SSL certificates, and email routing configured for the new structure.
- **Redirects.** Old vendor and legacy URLs redirected to their new equivalents so existing links, bookmarks and search rankings are preserved.
- **Ownership and handover.** Miku has already registered both domains in its own name and remains their sole owner. Hosting, database and DNS accounts are also held in Miku's name. All credentials and documentation delivered to Miku at handover.
- **Access control.** Role-based access for mikucentre.com so staff see only what their role requires.
- **Cutover and rollback.** A planned switchover outside peak hours, with a tested rollback path if anything fails.

2.3 SEO & GEO — Search Engine and Generative Engine Optimization

Search Engine Optimization (SEO) helps Miku rank on Google and other search engines. **Generative Engine Optimization (GEO)** makes Miku's information easy for AI assistants and AI-generated search answers to understand, trust and cite. Both are delivered as part of the build, covering the setup and foundations described below.

- **Keyword research** for parcel collection, university parcel and tracking searches in Malaysia.
- **Technical SEO.** Fast page speed and Core Web Vitals, clean URL structure, XML sitemap, robots rules, and mobile-first rendering.
- **On-page SEO.** Titles, descriptions, headings and internal linking for every public page.
- **Structured data.** Schema markup for the organisation, services, outlets and FAQs.
- **Local SEO.** Location pages and Google Business Profile guidance for Miku's collection point(s).
- **Migration protection.** A 301 redirect map from old URLs, so rankings carry over to the new site.
- **GEO foundations.** Question-and-answer content written to be quoted by AI assistants, a consistent brand and entity description across the site, an `llms.txt` file, and crawler access for AI search bots.
- **Measurement.** Google Search Console and analytics set up in Miku's accounts, plus a baseline report at launch.

Ranking positions and AI citations depend on factors outside any agency's control, including competition and search engine decisions, so we commit to the work and the baseline reporting rather than to specific rankings.

3. Deliverables

#	DELIVERABLE	ACCEPTED WHEN
1	System audit and inventory	A written list of every domain, system and account Miku uses today, and who controls each, is delivered (Appendix B).
2	Public website and Track & Trace on mikuparcel.com	All pages in Appendix A are live and the tracker returns correct status for test waybills.
3	Management domain on mikucentre.com	Private systems run on the domain with role-based access and no search indexing.
4	Data migration from Qylex Solution to Exabytes	Record counts and sample checks match the source data.
5	DNS, SSL, email and redirects	All domains resolve securely and old URLs redirect correctly.
6	SEO and GEO setup, with baseline report	Items in 2.3 are implemented and the baseline report is delivered.
7	Credentials, documentation and handover session	Miku confirms receipt of all accounts and documents.

4. Timeline & Milestones

FINAL HANDOVER DATE

25 December 2026

PHASE	ACTIVITY	INDICATIVE TIMING
1	Discovery and system audit	Week 1
2	Design and content structure	Weeks 1–2
3	Website build	Weeks 2–4
4	Data migration, Qylex Solution to Exabytes	Weeks 4–5
5	SEO and GEO setup	Weeks 5–6
6	Testing, cutover and go-live	Weeks 6–7
7	Buffer, fixes and final handover	Week 8

5. Client Responsibilities & Assumptions

To keep to the schedule, we ask Miku to provide the following promptly:

- Access to all current domains, hosting and systems, and written instruction to Qylex Solution and other vendors to cooperate with the data export and handover.
- Access to Miku's Exabytes account, where we understand the domains (mikuparcel.com and mikucentre.com), hosting and DNS are managed. This is to be confirmed in Discovery, and if DNS is managed elsewhere, Miku provides that access instead.
- The new database and hosting on Exabytes held in Miku's name, with Miku bearing the ongoing fees for these and the domains.
- Page content (text, collection rates and guide, location details, FAQs, internship information, Miku's history) and final brand assets.
- A named decision-maker who can review and approve work within three (3) business days.

We assume the tracking data held by Qylex Solution can be exported in a usable format and that the tracking features Miku offers today are the ones to be preserved.

6. Out of Scope

- New software features or systems beyond the pages and migration described above.
- Ongoing monthly SEO or GEO retainer, paid advertising, and content writing beyond setup.
- Third-party fees: domains, hosting, Exabytes usage, SSL and email licences.
- Mobile application development.
- Languages other than English.

7. Risks & Mitigations

RISK	MITIGATION
Qylex Solution is slow to release data or credentials.	Miku issues written instruction at kickoff. We request the export in Week 1 and build in the Week 8 buffer.
Downtime during DNS cutover.	Cutover planned outside peak hours, with lowered DNS TTLs beforehand and a tested rollback.
Ranking drop after moving URLs.	Full 301 redirect map and Search Console monitoring after launch.
Data loss or mismatch in migration.	Backups before migration, record-count and sample validation afterwards.
Late content or approvals.	Content deadlines agreed at kickoff. Delays may move go-live and are flagged early.

8. Support & Handover

Three (3) months of maintenance are included at no additional charge, starting on the final handover date of 25 December 2026 and ending on 25 March 2027.

- **Included:** bug fixes, security patches and updates, uptime monitoring, DNS, SSL and hosting configuration support, and minor content edits.
- **Not included:** new features or pages, redesigns, and ongoing SEO or GEO work.
- **Response:** reasonable response during business hours.
- **Handover:** a walkthrough session, written documentation, and delivery of all credentials to Miku.

After the three months, paid maintenance can be agreed separately if Miku wishes.

9. Investment & Payment

ITEM	DESCRIPTION	AMOUNT
Public website and Track & Trace	Section 2.1	
Centralisation and migration	Section 2.2	Included in total
SEO and GEO setup	Section 2.3	
Maintenance, 3 months	Section 8	Included, no charge
Total	**Fixed fee**	**RM4,300**

- The fee is subject to final confirmation by both parties and excludes third-party costs (Section 6) and any applicable taxes.
- The payment schedule will be confirmed together with the final fee.

10. Acceptance & Next Steps

- Miku reviews this proposal and confirms the open items: the fee, the payment schedule, and the signatory details.
- Both parties sign below, and afes. schedules the kickoff and issues the Week 1 information request.
- Work begins by 2 November 2026 to keep to the 25 December 2026 handover.

We look forward to working with you and delivering a platform Miku fully owns and can grow with. Please reach out with any questions in the meantime.

Yours sincerely,

For and on behalf of afes.

APPROVED BY

Rahimi Rusyuddin bin Mohd Nazri
Founder & Chief Executive Officer, afes.

Acknowledged & agreed by Miku

ACKNOWLEDGED BY

Muhammad Hamizan bin Ziani
Miku Parcel (designation to be confirmed)

Appendix A — Proposed Site Map (mikuparcel.com)

GROUP	PAGES
Home	Landing page with Track & Trace and call-to-action section
Collecting	Collection rates
Services	Track & Trace, complaint centre, claim support, outlet locator
Join Us	Internship
Info	About us, history (Miku's activities and achievements), FAQ, collection guide, terms of use

The final page list is confirmed in Discovery and depends on the content Miku can supply.

Appendix B — Current System Inventory

To be completed during Discovery (Week 1). Each row records what exists today and who controls it, so nothing is missed in the migration.

ASSET	CURRENT HOST / VENDOR	OWNER	ACTION
Domains (mikuparcel.com, mikucentre.com)	Exabytes (to be confirmed)	Miku	Keep, point to the new setup
Hosting	Exabytes (to be confirmed)	Miku	Consolidate under the two domains
DNS	Exabytes (to be confirmed)	Miku	Update records at cutover
Tracking data	Qylex Solution	To be confirmed	Migrate to Exabytes
Existing websites	To be confirmed	To be confirmed	Replace or redirect
Email	To be confirmed	To be confirmed	Reconfigure
